

# Addison Township Public Library

## New Building Update

Date: 3/16/2026



### Construction Progress and Updates


- Masonry work expected to be restarting in coming weeks (once weather shows no freezing nights)
- All interior partition walls are complete.
  - o Additional room was needed in the main floor storage area for an HVAC chase.
  - o Lockable storage room and electrical/server room added in basement based on input from TLN.
- Basic electrical installation complete (installation of electrical boxes and data ports). Additional electrical work has been discussed with builder for low voltage/communication wiring (feedback from TLN).
- Parking lot construction expected to resume once frost laws are lifted.
- Remaining exterior doors have been installed.

Options for usage compliance in basement are still under review. Southeast Commercial is currently reviewing an option for 2 egress windows and 1 stairwell. Waiting on cost estimations to present plan to the board.

### Committee Tasks

- TLN has been contacted to coordinate building electrical and data wiring.
  - ✓ Contacted TLN to schedule site visit.
  - ✓ TLN provided input on data port locations and future planning. Marked up drawings provided to the builder.
    - o Future site visit and follow-up will be scheduled around April/May.
- Coordinate transportation of reclaimed doors once building is fully sealed in with masonry and windows.
- Work with South East Commercial on interior finishes.


- Review potential options for exterior signage on the building (“Addison Township Public Library” sign) shown below.

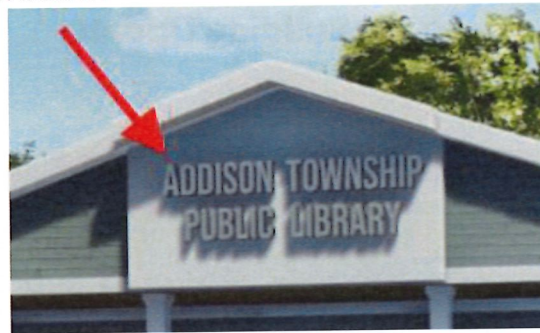

## Progress Pictures

### Doors



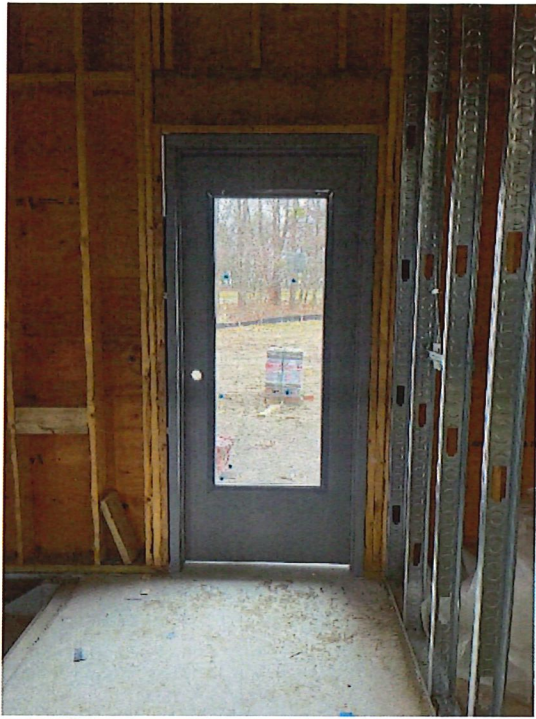

**Electrical and Entrance**





